

**Cambodia: The Upgrading of National Road No. 67 (NR67)  
(Siem Reap - Anlong Veng to Choam/Sa Ngam) Project**

**1. Project Information**

<b>Project Name:</b>	The Upgrading of National Road No. 67 (NR67) (Siem Reap - Anlong Veng to Choam/Sa Ngam) Project		
<b>Project No:</b>	CFA004-2022		
<b>Country:</b>	Cambodia		
<b>Sector(s)</b>	<ul style="list-style-type: none"> <li>- Transportation Linkage</li> <li>- Facilitate Trade and Investment</li> </ul>		
<b>Year of Approval:</b>	FY2016		
<b>Executing Agency:</b>	Ministry of Public Works and Transport (MPWT)		
<b>Scope of Works:</b>	<ul style="list-style-type: none"> <li>- upgrading the existing road pavement by using Asphaltic Concrete (AC) pavement and Reinforced Concrete (RC) pavement of approximately 134.68 kilometers</li> <li>- Improvement 7 intersections</li> <li>- Renovation of bridge structures and drainage systems in 25 locations and installing pipes to increase drainage efficiency in 8 locations</li> <li>- Improvement road facilities and road safety</li> </ul>		
<b>Budget Allocation:</b>	<b>Category</b>	<b>Loan Allocation (THB)</b>	<b>Contract Allocation (THB)</b>
	- Construction Works	904,500,000.00	904,500,000.00
	- Consulting Services	27,000,000.00	27,000,000.00
	- Administrative Cost	6,500,000.00	6,500,000.00
	- Contingencies	45,000,000.00	-
	<b>Total</b>	<b>983,000,000.00</b>	<b>938,000,000.00</b>
<b>Loan Condition:</b>	<ul style="list-style-type: none"> <li>- Interest Rate</li> <li>- Loan Period</li> <li>- Management Fee</li> <li>- Interest/ Principal Payment Dates</li> <li>- Civil Work Contractor and Consultant</li> <li>- Eligible goods, equipment and services of the project purchased from Thailand</li> <li>- Applicable Law</li> </ul>		
		1.5% per annum	
		25 years (including 7 years' grace period)	
		0.15% of the Loan amount	
		25 April and 25 October	
		Thai nationality	
		Not less than 50% of the total Project Cost	
		The laws of the Kingdom of Thailand	
<b>Construction Period:</b>	Approximate 24 months		

## 2. Project Objectives/ Benefits

<b>Objectives:</b>	To upgrade National Road No. 67 in Cambodia
<b>Benefits:</b>	<ul style="list-style-type: none"> <li>- Promoting connectivity between Thailand and Cambodia including consolidate the route network of Mekong Economic Cooperation Development Program</li> <li>- Cost saving, reduce travel time</li> <li>- Support the expansion of border trade, logistics. Investment and tourism in both Thailand and Cambodia</li> <li>- Promote tourism cooperation through joint tourism route</li> <li>- Encourage cultural exchange traditions between Thai and Cambodian</li> </ul>


## 3. Key Dates

<b>Loan Approval:</b>	August 26, 2022	<b>Loan Signing:</b>	November 4, 2022
<b>Effectiveness:</b>	January 24, 2023	<b>Restructuring (if any):</b>	-
<b>Original Closing:</b>	-	<b>Revised Closing (if any):</b>	-

## 4. Disbursement Summary as of May 2024

<b>Net Commitment:</b>	983,000,000.00 THB	<b>Revised Amount (if any):</b>	-
<b>Disbursed Amount:</b>	-	<b>Disbursed (April 2024):</b>	-
<b>Undisbursed Balance:</b>	938,000,000.00 THB	<b>Disbursement Ratio:</b>	-
<b>Cumulative Thai good and service usage:</b>	-	<b>Thai good and service usage (April 2024):</b>	-

Cumulative Disbursements (Quarterly/Calendar Year)

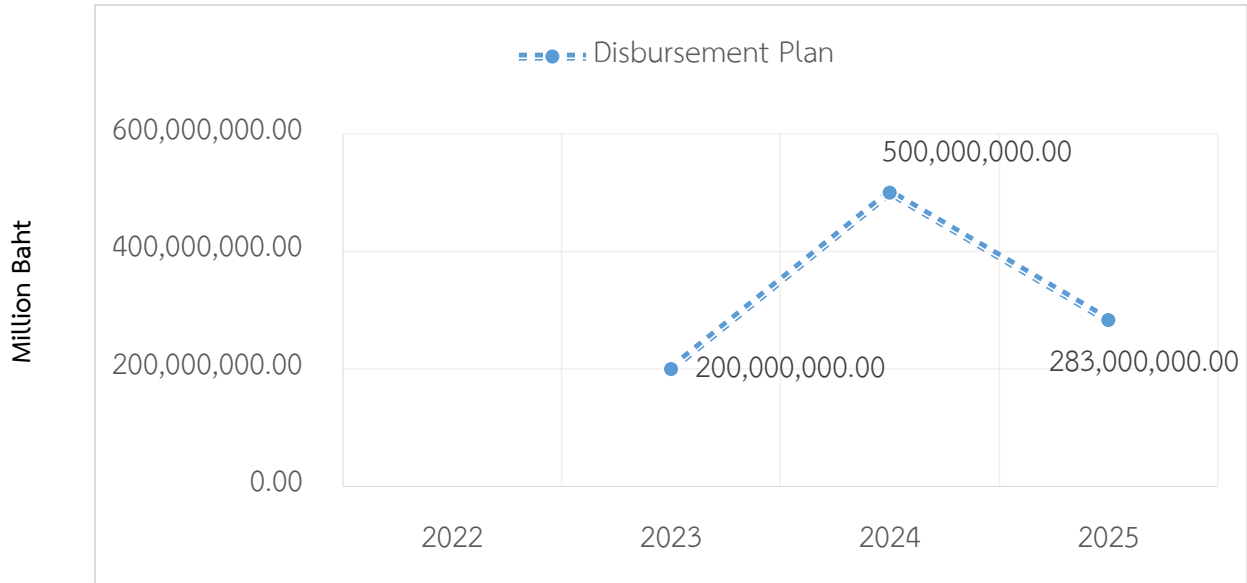

5. Project Implementation Status as of May 2024

	Status/ Details	Progress (%)
<b>Consulting Services:</b>	Under procurement procedure by Cambodia	-
- Name of Consultant(s):		
- Contract Signing Date:		
- Contract Amount:		
- Consultant Period:		
- Consultant Extension (if any):		
<b>Construction Works:</b>		
- Name of Contractor(s):		
- Contract Singing Date:		
- Contract Amount:		
- Construction Period:		
- Construction Extension (if any):		
- Variation Order (VO) (if any):		

6. Environmental and Social Safeguards Status

Stage	Documents	Status
Pre-construction	Evidence of Environmental/ Social Safeguards Letter Ref. No. 3947 MPWT, dated 7 Oct 2022	NEDA received the Evidence of Safeguards (Pre), supporting documents, IEE Report and Resettlement Plan already. (the letter No. 0549 MEF dated October 17, 2022)
During Construction		
Post-Construction		

7. Project images



Project map

8. Current Project Condition



Border checkpoint



NR67 Intersection



Damaged road



Damaged road
