

**Myanmar: Power System Development in Yangon City Project
(North Okkalapa and North Dagon Townships)**

1. Project Information

Project Name:	Power System Development in Yangon City Project (North Okkalapa and North Dagon Township)		
Project No:	MFA003/2020		
Country:	Myanmar		
Sector	Urban Development		
Year of Approval:	FY2020		
Executing Agency:	Ministry of Electricity and Energy (MOEE) and Yangon Electricity Supply Corporation (YESC)		
Scope of Works:	<ul style="list-style-type: none"> - Construction and improvement of 3 substations - Construction of transmission lines 52 km. - Construction and improvement of distribution line 91 km. - Construction of distribution transformer 		
Budget Allocation:	Category	Loan Allocation (THB)	Contract Allocation (THB)
	- Construction Works	1,339,817,011.00	1,339,817,011.00
	- Consulting Services	51,440,138.45	51,440,138.45
	- Contingencies	66,990,850.55	-
	Total	1,458,248,000.00	1,391,257,149.45
Loan Condition:	<ul style="list-style-type: none"> - Interest Rate 1.5% per annum - Loan Period 30 years (including 10 years' grace period) - Management Fee 0.15% of the Loan amount - Interest/ Principal Payment Dates 25 April and 25 October - Civil Work Contractor and Consultant Thai nationality 		

	- Eligible goods, equipment and services of the project purchased from Thailand	Not less than 50% of the total Project Cost
	- Applicable Law	The laws of the Kingdom of Thailand
Construction Period:	Approximate 24 months	

2. Project Objectives/ Benefits

Objectives:	Power System Development in Yangon City Project (North Okkalapa and North Dagon Townships)
Benefits:	<ul style="list-style-type: none"> - enhance the capacity of the power supply system to support the growth of electricity demand in North Okkalapa Township, Yangon City - improve power system reliability and efficiency - decrease operation and maintenance problems in the power system and increase the competitiveness of the country.


3. Key Dates

Loan Approval:	July 14, 2020	Loan Signing:	September 23, 2020
Effectiveness:	September 23, 2020	Restructuring (if any):	-
Original Closing:	September 22, 2025	Revised Closing (if any):	-

4. Disbursement Summary as of September 2024

Net Commitment:	1,458,248,000.00 THB	Revised Amount (if any):	-
Disbursed Amount:	-	Disbursed as of September 2024	-
Undisbursed Balance:	1,391,257,149.45 THB	Disbursement Ratio:	-
Cumulative Thai good and service usage:	-	Thai good and service usage (September 2024):	-

Disbursements Plan (Fiscal Year)

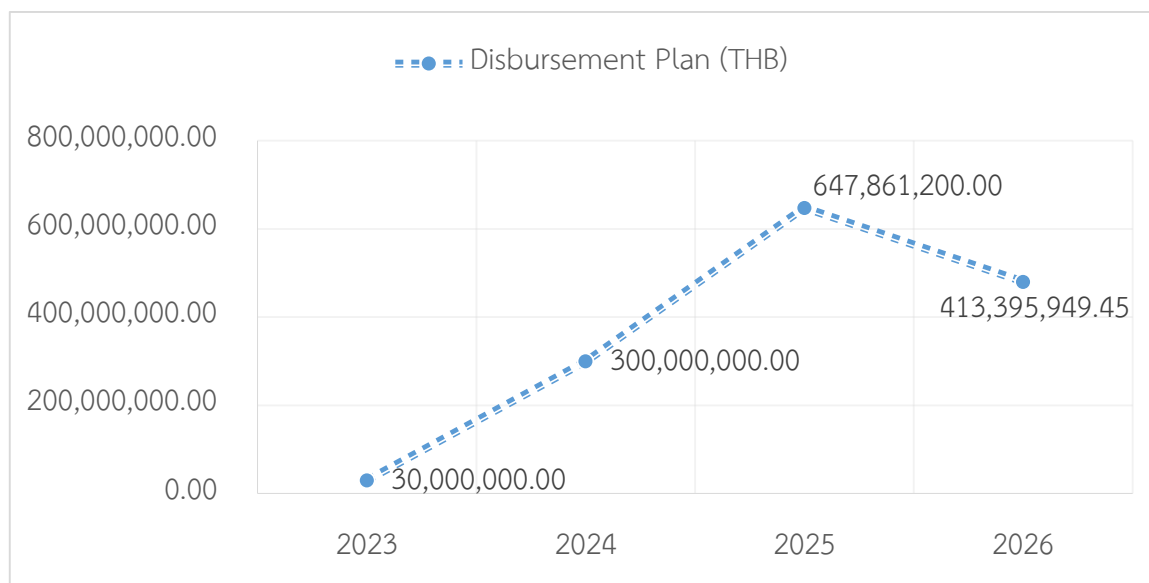

5. Project Implementation Status as of September 2024

	Status/ Details	Progress (%)
Consulting Services:	In progress: Executing Agency (Myanmar) is preparing the evaluation report of the consultant selection	-
- Name of Consultant(s):	-	
- Contract Signing Date:	-	
- Contract Amount:	-	
- Consultant Period:	-	
- Consultant Extension (if any):	-	
Construction Works:	-	-
- Name of Contractor(s):	-	
- Contract Singing Date:	-	
- Contract Amount:	-	
- Construction Period:	-	
- Construction Extension (if any):	-	
- Variation Order (VO) (if any):	-	

6. Environmental and Social Safeguards Status

Stage	Documents	Status
Pre-construction	-	-
During Construction		
Post-Construction		

7. Project Map



8. Project Area



Wai Bar Gi Substation



Shwe Pauk Kan Substation



North Okkalapa Substation



Existing Line
