

Cambodia: The Upgrading of National Road No. 67 (NR67) (Siem Reap - Anlong Veng to Choam/Sa Ngam) Project

1. Project Information

Project Name:	The Upgrading of National Road No. 67 (NR67) (Siem Reap - Anlong Veng to Choam/Sa Ngam) Project		
Project No:	CFA004-2022		
Country:	Cambodia		
Sector(s)	<ul style="list-style-type: none"> - Transportation Linkage - Facilitate Trade and Investment 		
Year of Approval:	FY2016		
Executing Agency:	Ministry of Public Works and Transport (MPWT)		
Scope of Works:	<ul style="list-style-type: none"> - upgrading the existing road pavement by using Asphaltic Concrete (AC) pavement and Reinforced Concrete (RC) pavement of approximately 134.68 kilometers - Improvement 7 intersections - Renovation of bridge structures and drainage systems in 25 locations and installing pipes to increase drainage efficiency in 8 locations - Improvement road facilities and road safety 		
Budget Allocation:	Category	Loan Allocation (THB)	Contract Allocation (THB)
	- Construction Works	904,500,000.00	904,500,000.00
	- Consulting Services	27,000,000.00	27,000,000.00
	- Administrative Cost	6,500,000.00	6,500,000.00
	- Contingencies	45,000,000.00	-
	Total	983,000,000.00	938,000,000.00
Loan Condition:	<ul style="list-style-type: none"> - Interest Rate - Loan Period - Management Fee - Interest/ Principal Payment Dates - Civil Work Contractor and Consultant - Eligible goods, equipment and services of the project purchased from Thailand - Applicable Law 		
		1.5% per annum	
		25 years (including 7 years' grace period)	
		0.15% of the Loan amount	
		25 April and 25 October	
		Thai nationality	
		Not less than 50% of the total Project Cost	
		The laws of the Kingdom of Thailand	
Construction Period:	Approximate 24 months		

2. Project Objectives/ Benefits

Objectives:	To upgrade National Road No. 67 in Cambodia
Benefits:	<ul style="list-style-type: none"> - Promoting connectivity between Thailand and Cambodia including consolidate the route network of Mekong Economic Cooperation Development Program - Cost saving, reduce travel time - Support the expansion of border trade, logistics. Investment and tourism in both Thailand and Cambodia - Promote tourism cooperation through joint tourism route - Encourage cultural exchange traditions between Thai and Cambodian


3. Key Dates

Loan Approval:	August 26, 2022	Loan Signing:	November 4, 2022
Effectiveness:	January 24, 2023	Restructuring (if any):	-
Original Closing:	-	Revised Closing (if any):	-

4. Disbursement Summary as of September 2024

Net Commitment:	983,000,000.00 THB	Revised Amount (if any):	-
Disbursed Amount:	-	Disbursed (September 2024):	-
Undisbursed Balance:	938,000,000.00 THB	Disbursement Ratio:	-
Cumulative Thai good and service usage:	-	Thai good and service usage (September 2024):	-

Cumulative Disbursements (Quarterly/Calendar Year)

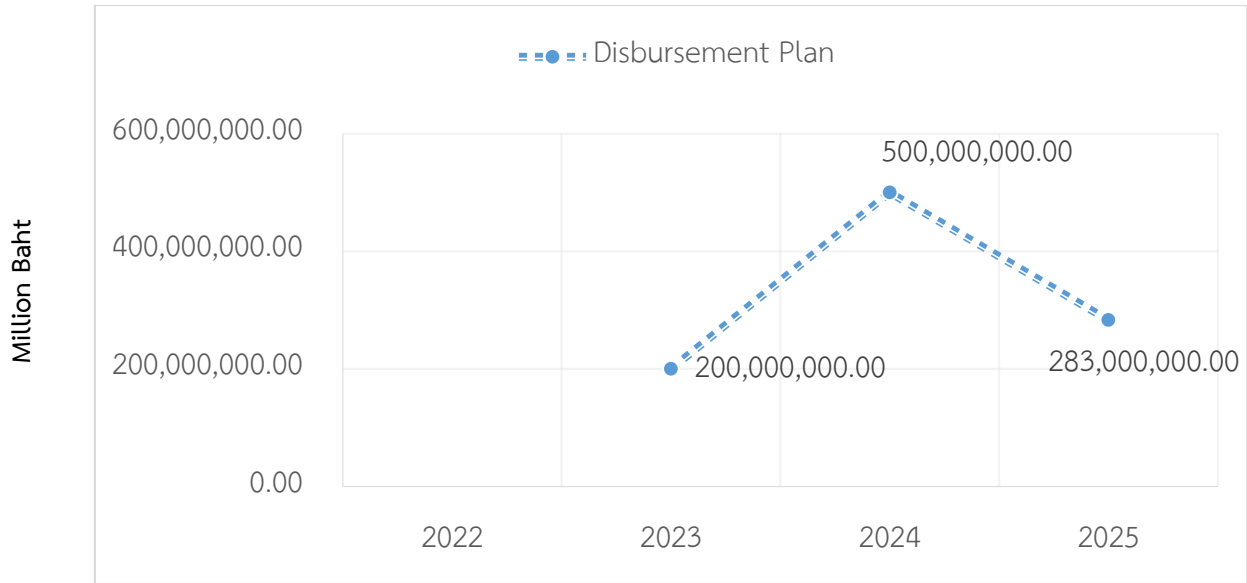

5. Project Implementation Status as of September 2024

	Status/ Details	Progress (%)
Consulting Services:	Under procurement procedure by Cambodia	-
- Name of Consultant(s):		
- Contract Signing Date:		
- Contract Amount:		
- Consultant Period:		
- Consultant Extension (if any):		
Construction Works:		
- Name of Contractor(s):		
- Contract Singing Date:		
- Contract Amount:		
- Construction Period:		
- Construction Extension (if any):		
- Variation Order (VO) (if any):		

6. Environmental and Social Safeguards Status

Stage	Documents	Status
Pre-construction	Evidence of Environmental/ Social Safeguards Letter Ref. No. 3947 MPWT, dated 7 Oct 2022	NEDA received the Evidence of Safeguards (Pre), supporting documents, IEE Report and Resettlement Plan already. (the letter No. 0549 MEF dated October 17, 2022)
During Construction		
Post-Construction		

7. Project images



Project map

8. Current Project Condition



Border checkpoint



NR67 Intersection



Damaged road



Damaged road
